PRM FASHIONS PVT. LTD

SS SFB-5, KARNAPHULI EPZ, NORTH PATENGA, Chittagong
(22.276409N, 91.796774E)

06th April ,2017




ACCORD
on Fire and Building Safety in Bangladesh

Observation

ACCORD
on Fire and Building Safety in Bangladesh

Discrepancies between provided drawing and as-built condition.

ACCORD
on Fire and Building Safety in Bangladesh

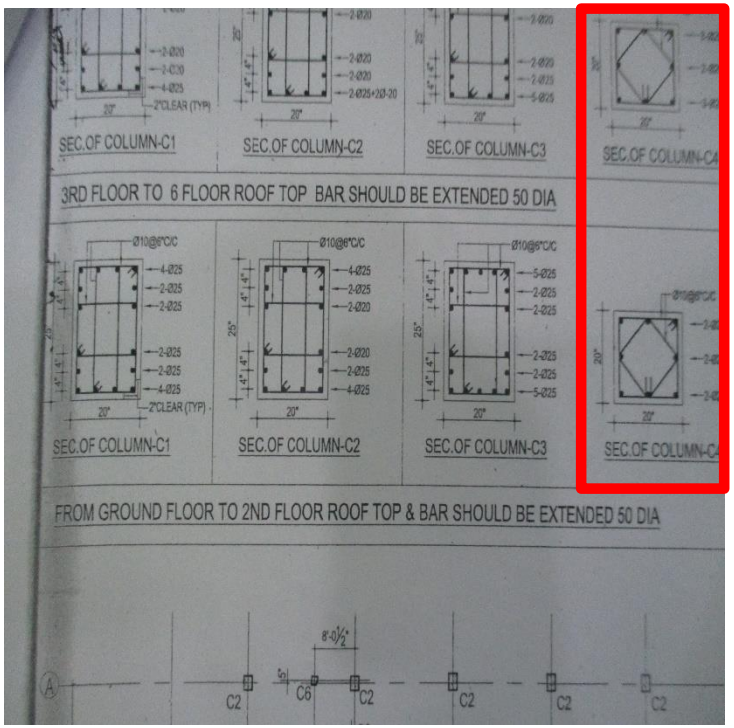



C4 type column shown in as built structural drawing but not found on site. Moreover 8 Nos. of plastic water tanks found at roof which were not shown in architectural drawing.

Observation:(Production Building)

ACCORD
on Fire and Building Safety in Bangladesh

Absence of Load plan

ACCORD
on Fire and Building Safety in Bangladesh





No load plan was observed at the building . Factory engineer require to produce load plan for all floors considering floor loading capacity.

Observation:(Production Building)

ACCORD
on Fire and Building Safety in Bangladesh

Problems Observed

Production Building

Item 1: Discrepancies between provided drawing and as-built condition.

Item 2: Absence of Load plan

Priority Actions

Item No.	Observation	Recommended Action Plan	Recommended Timeline
1	Discrepancies between provided drawing and as-built condition.	Building Engineer required to prepare As –Built drawings reflecting the actual condition.	**6-weeks**
2	Absence of Load Plan	Produce and actively manage a load plan for all floor plates within the factory giving consideration to floor capacity and column capacity	**6-weeks**
3	Absence of Load Plan	Continue to implement load plan	**6-months**
