Issue	**1**
Factory ID	**26326**
Date of Issue	**19-May-2026**

Eclipse Sports (Pvt.) Ltd.

Pakistan ACCORD for Health and Safety in the Garment and Textile Industry

Raypur Stop, Wazirabad Road,
51310 Sialkot
Punjab Pakistan

Latitude: [32.477965], longitude: [74.427812]
Date of inspection: 11-Mar-2026

Structural Safety Inspection Report

Observations & Actions



Authors	**Haris Mahmood**
Reviewed by	**Ausama Iqbal**
Approved by	**Colm Quinn**

Pakistan Accord Initial Safety Inspection Report

About this report:

This report has been prepared by the Health and Safety Accord Pvt Ltd after visiting the factory on 11-03-2026 as part of the inspection and remediation program of the Pakistan Accord on Health and Safety in the Textile and Garment Industry. The purpose of the report is to provide key findings and identify related safety improvements needed at the inspected factories. This inspection report may not identify minor deficiencies, which may be further addressed as part of follow-up inspections.

In addition, while this round of initial inspections covers fire, electrical and structural safety, the Pakistan Accord intends to include inspections on boiler safety and hazardous material in later rounds.

This report will serve to facilitate discussions between the Pakistan Accord, the factories and the responsible brands that source from this facility about the remediation requirements. An implementation schedule shall be developed by the factory in the form of a Corrective Action Plan (CAP) to remediate each of the findings identified in the inspection report, including timelines and cost estimates, for approval by the Chief Safety Officer (CSO).

Applied Standards:

This safety assessment was conducted by the Pakistan Accord with reference to the Pakistan Accord Building Standard.

Contents

1. Executive Summary 4
2. Building Extents 5
   2.1 Structural System 13
3. Documentation 16
4. Structural Safety Measures 17
5. Remediation Support 18
   5.1 Engineering Support 18
6. Other Damage/Defects 19
   6.1 Health and Safety 19
7. Structural Documentation 21
   7.1 Documentation unavailable 21
   7.2 Lack of safe load plans 22
8. Assessment Limitations and Assumptions 23

1. Executive Summary

On 11-Mar-2026, Haris Mahmood and Owais Raza on behalf of the Pakistan Accord carried out an initial structural inspection for Eclipse Sports (Pvt.) Ltd., a factory at the address and coordinates given on the cover page of this report. The inspection was carried out in accordance with the Pakistan Accord Building standards.

We met with Mr. Akbar Khan (Manager Compliance), Mr. Khurram Rasheed (Compliance Consultant) and other staff members of Eclipse Sports (Pvt.) Ltd. The assessment was conducted as a part of an overall Structural, Fire, and Electrical initial inspection.
The factory operates in single general shift. Factory employs approximately 70 workers with approximately 7% female representation.
The factory comprises of a main building in which two floors (3rd and 4th) were rented to Eclipse Sports (Pvt.) Ltd on a tenancy basis, rest of the floors were occupied by a surgical instruments manufacturing company. During the inspection, the building highlighted in blue in Figure 1.1 was surveyed with the site boundary indicated in red.

- **Main Building** is mainly a five-storey (G+4) building. The structural system of the building is a combination of RC moment resisting frame system and structural steel shed. The building is used for surgical instruments manufacturing (Ground, First and Second Floors), cutting, finishing, printing, packing, guesthouse, sublimation, heat-transfer (Third floor), Fabric Store, Kitchen, Open-gymnasium, solar Inverter, steamer (Fourth Floor) and workers residence, birds cages, water tank (Roof). The construction year of the building is 2014.

We were presented with the site layout plan of the building. For further details, refer to Table 2 of the documentation of this report.
There is a health and safety concern including the lack of edge protection / safety handrail on the internal staircases of the main building, which should be addressed immediately. For further details, refer to Section 6 of this report.
A summary of main concerns identified on-site during the assessment (non-exhaustive) that should be actioned are as follows:

- No safe load plans were posted in any of the floor of the main building
- No documentation (As-Built Architectural and Structural Drawings) was available

We see no reason to suspend operations in the facility due to these concerns.

Our Limitations and Assumptions are also noted at the end of this report.

For detailed analysis of the above, please refer to the full inspection report below, which further details each issue, and also includes photographs. Further actions with associated priorities and timeframes are also detailed with each issue. Please note that these actions should be completed as soon as practically possible and certainly within the timeframe noted.

2. Building Extents

Table 1: Building Summary

Building	Use	No. of stories	Year of construction	Structural system	Roof structural system	Any Extension / modifications	Engineer access issues
Main Building	Surgical instruments manufacturing (Ground, First and Second Floors) Cutting, finishing, printing, packing, guesthouse, sublimation, heat-transfer (Third floor) Fabric Store, Kitchen, Open-gymnasium, solar Inverter, steamer (Fourth Floor) Worker's residence, birds cages, water tank (Roof)	Five (G+4)	2014	Combination of RC moment resisting frame system and structural steel shed	-	-	-



Figure 1.1. Site plan (Satellite view) – Red dashed line indicates site boundary, highlighted area (blue) indicates building inspected

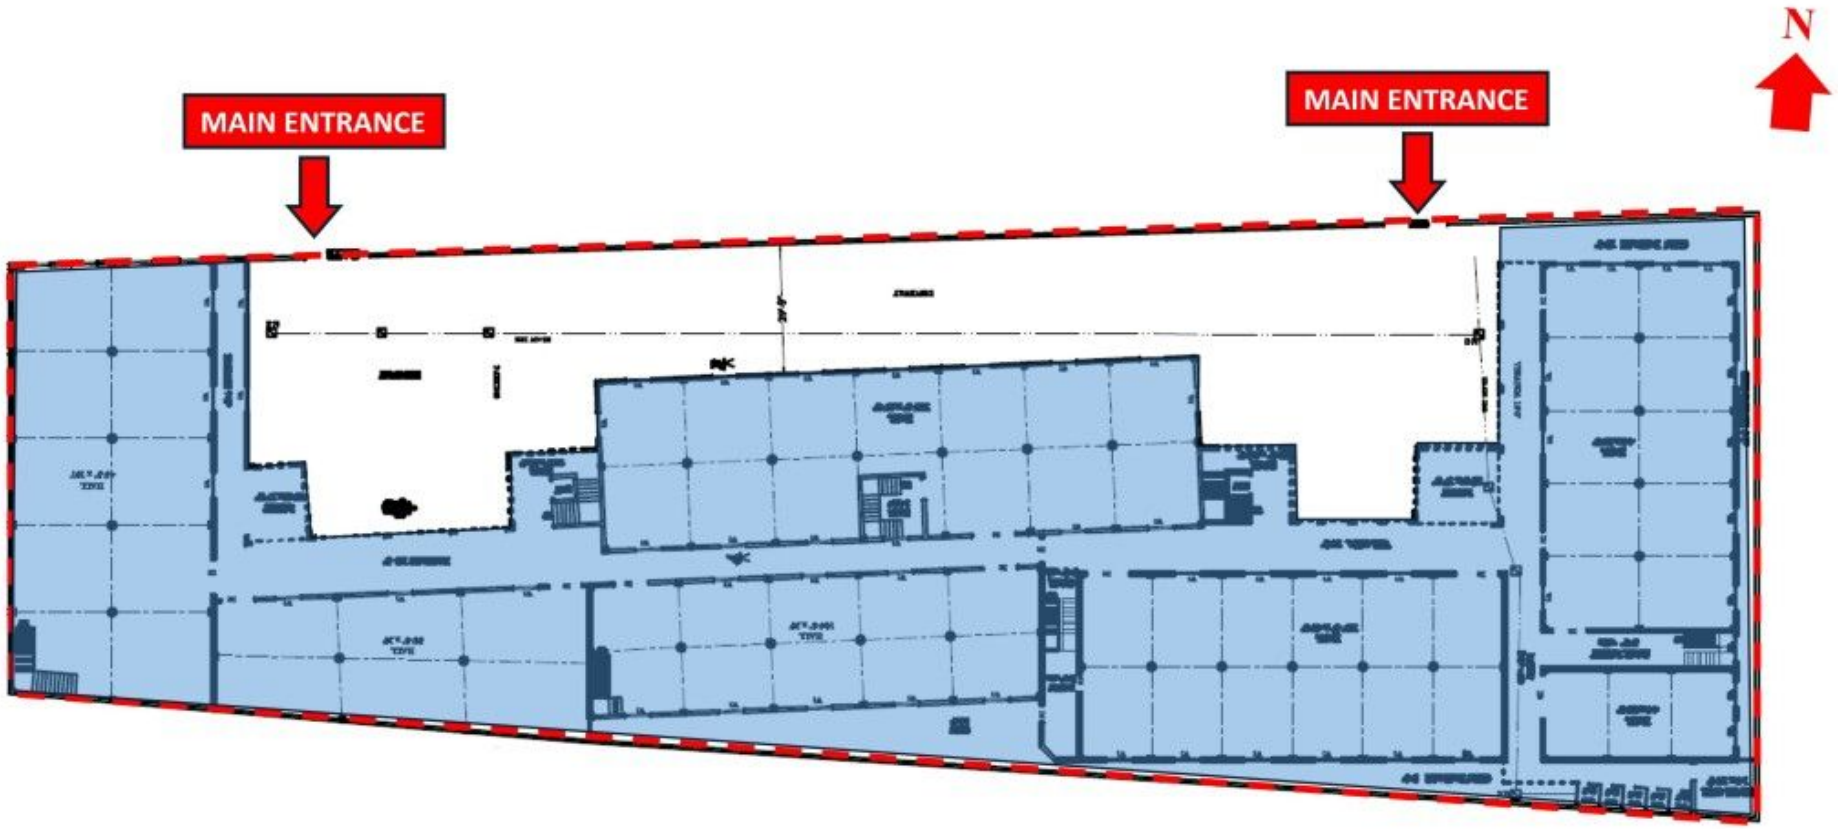


Figure 1.2. Site layout plan - Red dashed line indicates site boundary, highlighted area (blue) indicates building inspected



Figure 1.3. Front Elevation of Main Building



Figure 1.4. Surgical Instruments Manufacturing at Ground level of Main Building



Figure 1.5. Surgical Instruments Manufacturing at Ground level of Main Building



Figure 1.6. Offices at Ground Floor Level of Main Building



Figure 1.7. Surgical Instruments Manufacturing at First Floor of Main Building



Figure 1.8. Surgical Instruments storage at first floor of Main Building



Figure 1.9. Surgical Instruments Inventory at First Floor of Main Building



Figure 1.10. Surgical Instruments checking area at first floor of Main Building



Figure 1.11. Surgical Instruments storage at Second floor of Main Building



Figure 1.12. Display Room and Conference Area at Third Floor of Main Building



Figure 1.13. Printing at Third floor of Main Building



Figure 1.14. Stitiching at Third Floor of Main Building



Figure 1.15. Checking Tables at Third Floor of Main Building



Figure 1.16. Packing at Third Floor of Main Building



Figure 1.17. Fabric Storage at Fourth Floor of Main Building



Figure 1.18. Kitchen at Fourth Floor of Main Building



Figure 1.19. Area for Open-Gymnasium at 4th Floor



Figure 1.20. Sleeping Area at Roof of Main Building



Figure 1.21. Bird Cages at Roof of Main Building

2.1 Structural System

Building	Main Building
Stability system	RC moment resisting frame system and structural steel shed
Column size (m)	G+1 Portion: 0.350 x 0.350 G+2 Portion: 0.350 x 0.350 G+3 Portion: 0.410 x 0.410 G+4 Portion: 0.410 x 0.410
Grid (m)	G+1 Portion: 6.25 x 5.05 G+2 Portion: 6.25 x 5.05 (max.) G+3 Portion: 6.51 x 5.31 (max.) G+4 Portion: 6.25 x 5.05
Primary beam size (m)	G+1 Portion: 0.350 x 0.320 G+2 Portion: 0.350 x 0.320 G+3 Portion: 0.350 x 0.320, 0.410 x 0.320 G+4 Portion: 0.410 x 0.320
Secondary beam size (m)	-
Slab depth (m)	0.150 (Assumed)
Finishes depth (m)	0.100 (Assumed)
Ceiling height (m)	G+1 Portion: G to 1st Floor = 3.2, 3.5 1st Floor to Roof = 3.5 G+2 Portion: Typical on each Floor = 3.2 G+3 Portion: G to 1st = 4.0 Typical on other Floors = 3.2 G+ 4 Portion: Typical on each Floor = 3.2

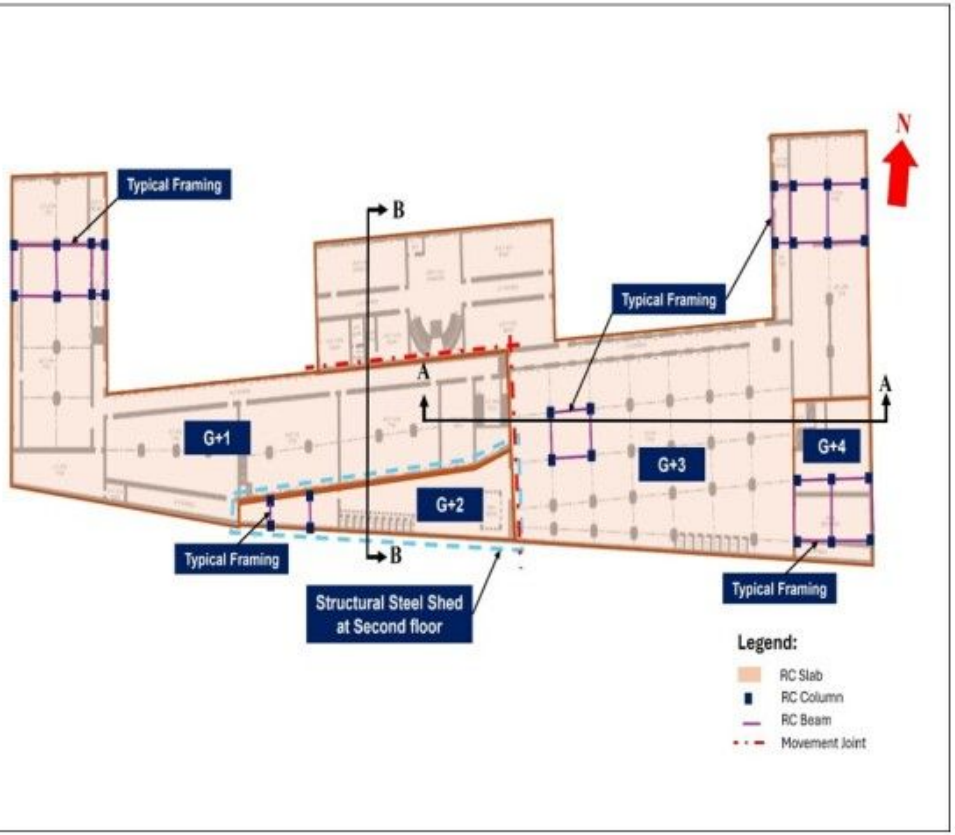


Figure 1.22. Typical Floor Framing Plan of the Main Building


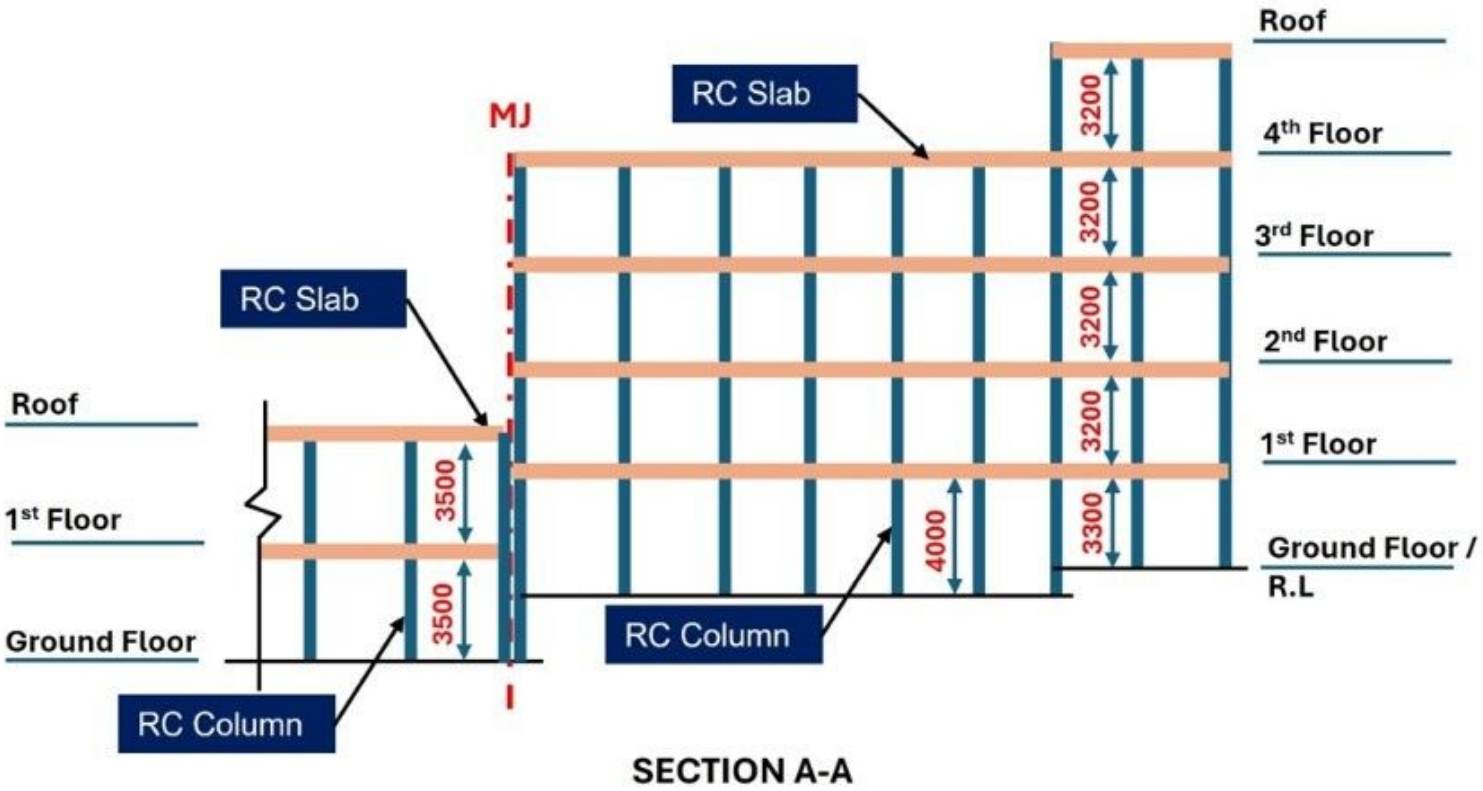


Figure 1.23. Section A-A of the Main Building

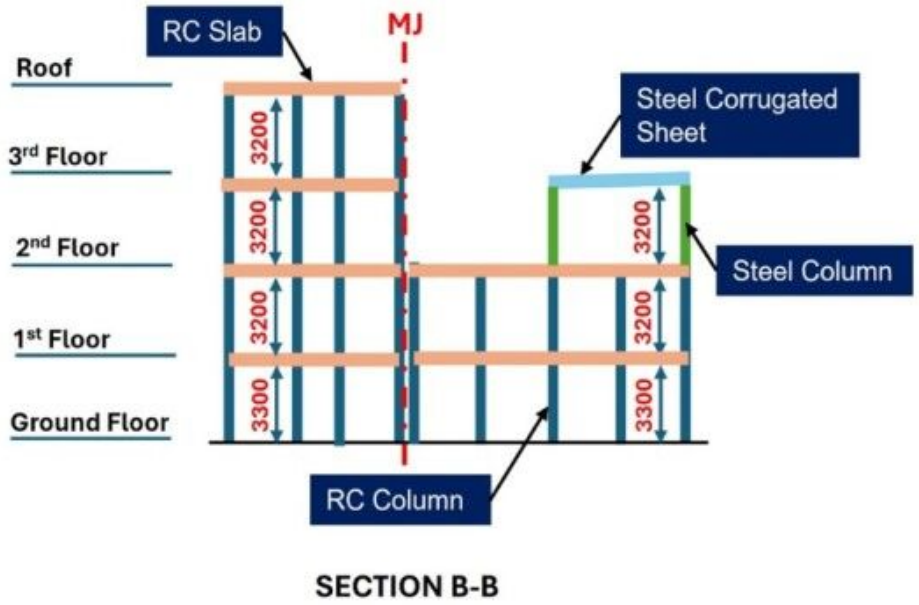

Structural System Notes

Column size is the structural dimension and excludes render thickness
Grid measurements are from centre of column to centre of column
Beam sizes do not include slab depth

Figure 1.24. Section B-B of the Main Building

3. Documentation

This table outlines the documentation details provided by the factory.

Table 2 – Documentation

Building	Site layout	Approved layout / permit	Geotech report	Design drawings	As-built drawings	Loading plans	Stability certificate	Inspection reports	Materials testing
Main Building	Yes	No	No	No	No	No	No	No	No

4. Structural Safety Measures

During our structural site inspection of Eclipse Sports (Pvt.) Ltd., a number of structural issues were identified.

It is essential to address these structural safety issues promptly to enhance safety and compliance within Eclipse Sports (Pvt.) Ltd.. Each issue should be carefully evaluated, and the recommendations provided in this report should be followed diligently to rectify these concerns. The safety and well-being of the factory's employees depend on these corrective actions. Where issues are identified in the report, they are grouped by topic, not in order of importance. Please note that these actions should be completed as soon as practically possible and certainly within the timeframe noted.

Recommendations in this report are prioritized as follows:

Immediate: These recommendations address safety and compliance concerns that require immediate attention.

Medium term (within approx. 6-weeks): Recommendations of high importance but needing slightly more time to implement.

Longer term (within approx. 6-months): Important recommendations that require a longer period to fully implement or that enhance long-term safety and efficiency.

Table 3 Summary of issues by building:

Building	Potential Overstress	Structural system	Cracking	Loading	Other damage and defects	Structural documentation
Main Building	-	-	-	-	Health and Safety – Lack of Edge Protection	Documentation Unavailable Lack of safe Load Plans

5. Remediation Support

5.1 Engineering Support

Some items in the Corrective Action Plan (CAP) will require remediation by a qualified Engineer. Please refer to the Remediation Plan for guidance on which tasks can be completed using internal resources and which require engineering support. F-202604-065256

Timeline	Remediation Plan
Medium Term CAP-0077222	Factories should begin remediation of CAP items—such as surface cracks or non-structural repairs using internal resources, where available. For remediation based on engineering assessments, detailed engineering assessments, or structural strengthening, engagement of a qualified Structural Engineer is required.

6. Other Damage/Defects

6.1 Health and Safety

This refers to the Main Building.
The internal staircases of the building are missing an edge protection/safety handrail. Missing edge protection presents a risk of potential injury resulting from slip, trip of fall from the stairs, while accessing. This is a Health and Safety Concern. F-202604-065317

Timeline	Remediation Plan
Immediate CAP-0077291	Provide adequate edge protection / safety handrail on the staircases, and on any other part of the factory with the same issue.



Figure 2.1 - Locations of Stairs with missing edge protection / Safety Handrail



Figure 2.3 - Internal Stairs with missing handrail edge protection / safety handrail



Figure 2.2 - Internal Stairs with missing handrail edge protection / safety handrail

7. Structural Documentation

7.1 Documentation unavailable

Following documents were unavailable:

- As-Built Architectural drawings of the Main Building
- Structural Drawings of the Main Building
- Approved site layout plan of the Main Building F-202604-065257

Timeline	Remediation Plan
Longer Term CAP-0077223	Building Structural Engineer to carry out on-site survey, collect information and produce accurate and complete As-Built documentation.

7.2 Lack of safe load plans

No safe load plans were posted on any of the floor in the main building of the factory. F-202604-065258

Timeline	Remediation Plan
Longer Term CAP-0077224	Building Structural Engineer to review design documentation to confirm load capacity of the structure
Longer Term CAP-0077225	Develop safe load plans and submit to Pakistan Accord for review.
Longer Term CAP-0077226	Factory to post safe load plans on all floors.

8. Assessment Limitations and Assumptions

The information in this report was obtained during an inspection of the facility and based on information provided by factory management. It has not been possible to provide independent verification for all the information and data collected, and therefore, the Accord cannot accept general responsibility for omissions or errors arising from inaccuracies in this report from the information obtained.

The findings and recommendations in this report are not intended to imply, guarantee, ensure or warrant compliance with any government regulations. Additionally, the results do not imply in any way that compliance with the findings or recommendations as stated in this report will eliminate all hazards, risks or exposures or that hazards, risks or exposures not referred to in this report do not exist. Compliance with the findings and recommendations stated in this report does not relieve the factory owner from obligation to comply with specific project requirements, industry standards, or the provisions of any local government regulations.

Except as otherwise noted within this report, other systems or services were not viewed or tested during the assessment and are therefore similarly excluded from this report. We have not assessed any parts of the structure / building fabric / services which are covered, unexposed or inaccessible and we are therefore unable to report that any such part of the property is free from defect.

The observations in this report are based on the engineering judgement of the engineer at the time of the inspection.
