Issue	**1**
Factory ID	**26347**
Date of Issue	**07-Apr-2026**

Select Enterprise

P-204, Arshad Town, Darbar Street Rajbah Road
Faisalabad
Punjab Pakistan

Latitude: [31.424016], longitude: [73.025898]
Date of inspection: 10-Mar-2026

Structural Safety Inspection Report

Observations & Actions



Authors	**Muhammad Asim**
Reviewed by	**Talha Akram Khan**
Approved by	**Paul Rigby**

Pakistan Accord Initial Safety Inspection Report

About this report:

This report has been prepared by the Health and Safety Accord Pvt Ltd after visiting the factory on 10-03-2026 as part of the inspection and remediation program of the Pakistan Accord on Health and Safety in the Textile and Garment Industry. The purpose of the report is to provide key findings and identify related safety improvements needed at the inspected factories. This inspection report may not identify minor deficiencies, which may be further addressed as part of follow-up inspections.

In addition, while this round of initial inspections covers fire, electrical and structural safety, the Pakistan Accord intends to include inspections on boiler safety and hazardous material in later rounds.

This report will serve to facilitate discussions between the Pakistan Accord, the factories and the responsible brands that source from this facility about the remediation requirements. An implementation schedule shall be developed by the factory in the form of a Corrective Action Plan (CAP) to remediate each of the findings identified in the inspection report, including timelines and cost estimates, for approval by the Chief Safety Officer (CSO).

Applied Standards:

This safety assessment was conducted by the Pakistan Accord with reference to the Pakistan Accord Building Standard.

Contents

1. Executive Summary 4
2. Building Extents 5
   2.1 Structural System 11
3. Documentation 14
4. Structural Safety Measures 15
5. Remediation Support 16
   5.1 Engineering Support 16
6. Other Damage/Defects 17
   6.1 Health and Safety 17
7. Structural Documentation 18
   7.1 Documentation unavailable 18
   7.2 Lack of safe load plans 19
8. Assessment Limitations and Assumptions 20

1. Executive Summary

On 10-Mar-2026, Ausama Iqbal and Muhammad Asim on behalf of the Pakistan Accord carried out an initial structural inspection for Select Enterprise, a factory at the address and coordinates given on the cover page of this report. The inspection was carried out in accordance with the Pakistan Accord Building standards.

We met with factory management representative Mr. Muhammad Shabbir (Owner), Mr. Mohsin Siddique (HR manager), and other staff members of Select Enterprise.
The factory operates in a general single shift. Approximately 45 workers operate in the factory with 2 workers being females.
The factory comprises of one main building owned by Select Enterprise. During the inspection, the area highlighted in blue in Figure 1.1 was inspected, with the site boundary indicated in red.

- **Main Building** is mainly a two storey (Ground+1) building and locally three storey (Ground + Mezzanine +1, Ground +2) building. The structural system of the building consists of an RC moment-resisting frame system. The roof structural system consists of load bearing brick masonry wall supporting RC slab. The building is used for solar panels, storage (roof), stitching, pressing, packing, meeting room (first floor), prayer area, storage (mezzanine), warehouse, store, offices and cutting (ground floor). The construction year of the building is 2017.

Incomplete site layout was provided at the factory. For further details, refer to table 2 of the documentation.
There is one Health and Safety issue which should be addressed immediately, regarding the unprotected opening at the front side of the lift in the main building. Further details are provided in section 6.
A summary of concerns identified on-site during the assessment (non-exhaustive) that should be actioned are as follows:

- Safe load plans were not posted on any of the floors of the main building.

We see no reason to suspend operations in the facility due to these concerns, subject to the actions identified being addressed within the specified timeframes.
Our Limitations and Assumptions are also noted at the end of this report.

For detailed analysis of the above, please refer to the full inspection report below, which further details each issue, and also includes photographs. Further actions with associated priorities and timeframes are also detailed with each issue. Please note that these actions should be completed as soon as practically possible and certainly within the timeframe noted.

2. Building Extents

Table 1 - Building Summary

Building	Use	No. of stories	Year of construction	Structural System	Roof structure system	Any extension/Modification	Engineer access issue
Main Building	Solar panels, storage (roof), stitching, pressing, packing, meeting room (first floor), prayer area, storage (mezzanine), warehouse, store, offices and cutting (ground floor).	Mainly a two storey (Ground+1) locally three storey (Ground + Mezzanine +1, Ground +2)	2017	RC moment-resisting frame system.	Load bearing brick masonry wall supporting RC slab.	-	-



Figure 1.1. Site plan (Satellite View) – Red dashed line indicates site boundary, highlighted area (blue) indicates buildings inspected

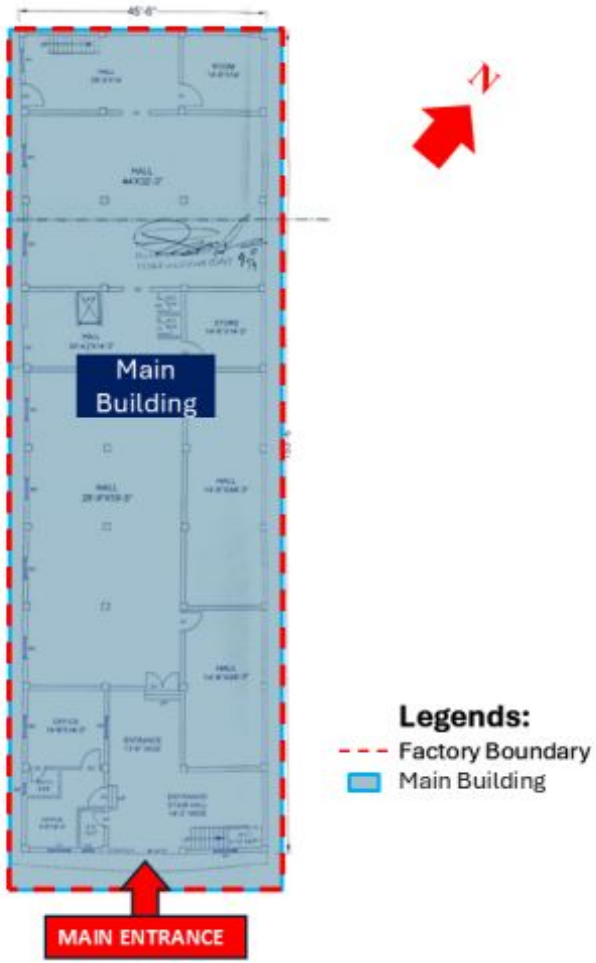


Figure 1.2. Site layout Plan; Red dashed line indicates site boundary, highlighted area indicates buildings inspected



Figure 1.3. Main Building - Front elevation of the building



Figure 1.4. Main Building - Side Elevation



Figure 1.5. Main Building - Solar panles at roof level.



Figure 1.6. Main Building - Storage at roof



Figure 1.7. Main Building - Stitching at first floor.



Figure 1.8. Main Building - Pressing at first floor.



Figure 1.9. Main Building - Packing at first floor.



Figure 1.10. Main Building - Prayer area at mezzanine floor.



Figure 1.11. Main Building - Storage at mezzanine floor.



Figure 1.12. Main Building - Storage at ground floor.



Figure 1.13. Main Building - Cutting at ground floor.

2.1 Structural System

Building	Main Building
Stability System	RC moment resisting frame system.
Column Size (m)	0.30x0.30
Grid (m)	4.63x4.63 (Max grid)
Primary Beam Size (m)	0.33x0.32
Secondary Beam Size (m)	-
Slab Depth (m)	0.15
Finishes Depth (m)	0.10
Floor to Ceiling Height (m)	4.70/4.40 (Ground - First) 2.225 (Ground - Mezzanine) 3.40 (First - Roof)

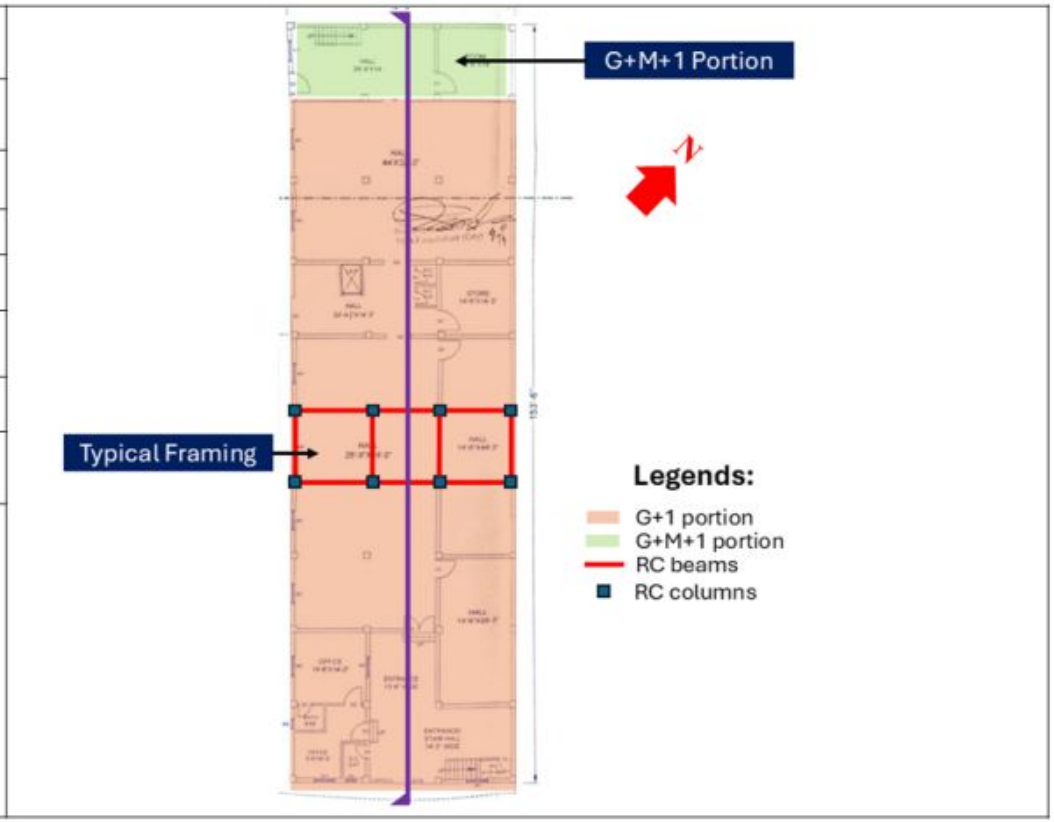


Figure 1.14. Typcial floor framing plan detail of main building

Building	Main Building
Stability System	Load bearing brick masonry wall supporting RC slab
Column Size (m)	-
Grid (m)	-
Primary Beam Size (m)	-
Secondary Beam Size (m)	-
Slab Depth (m)	0.15
Finishes Depth (m)	0.10
Floor to Ceiling Height (m)	3.0 (Roof)

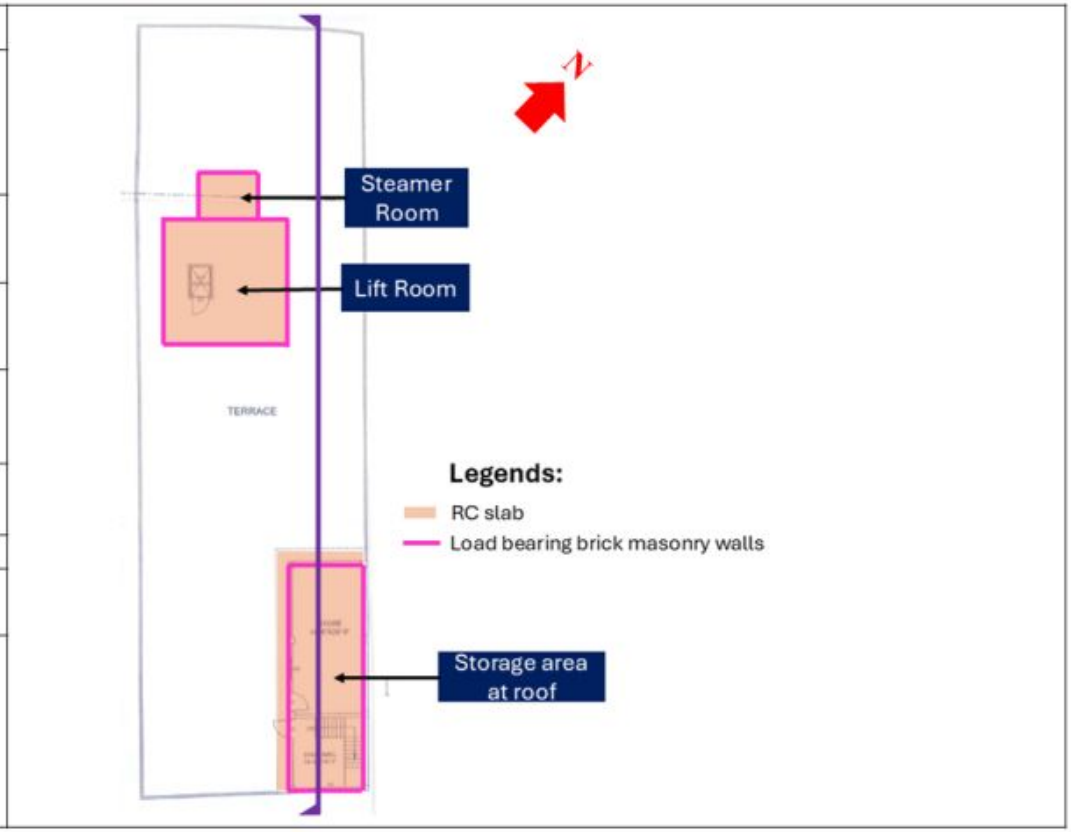


Figure 1.15. Top roof framing plan detail of main building

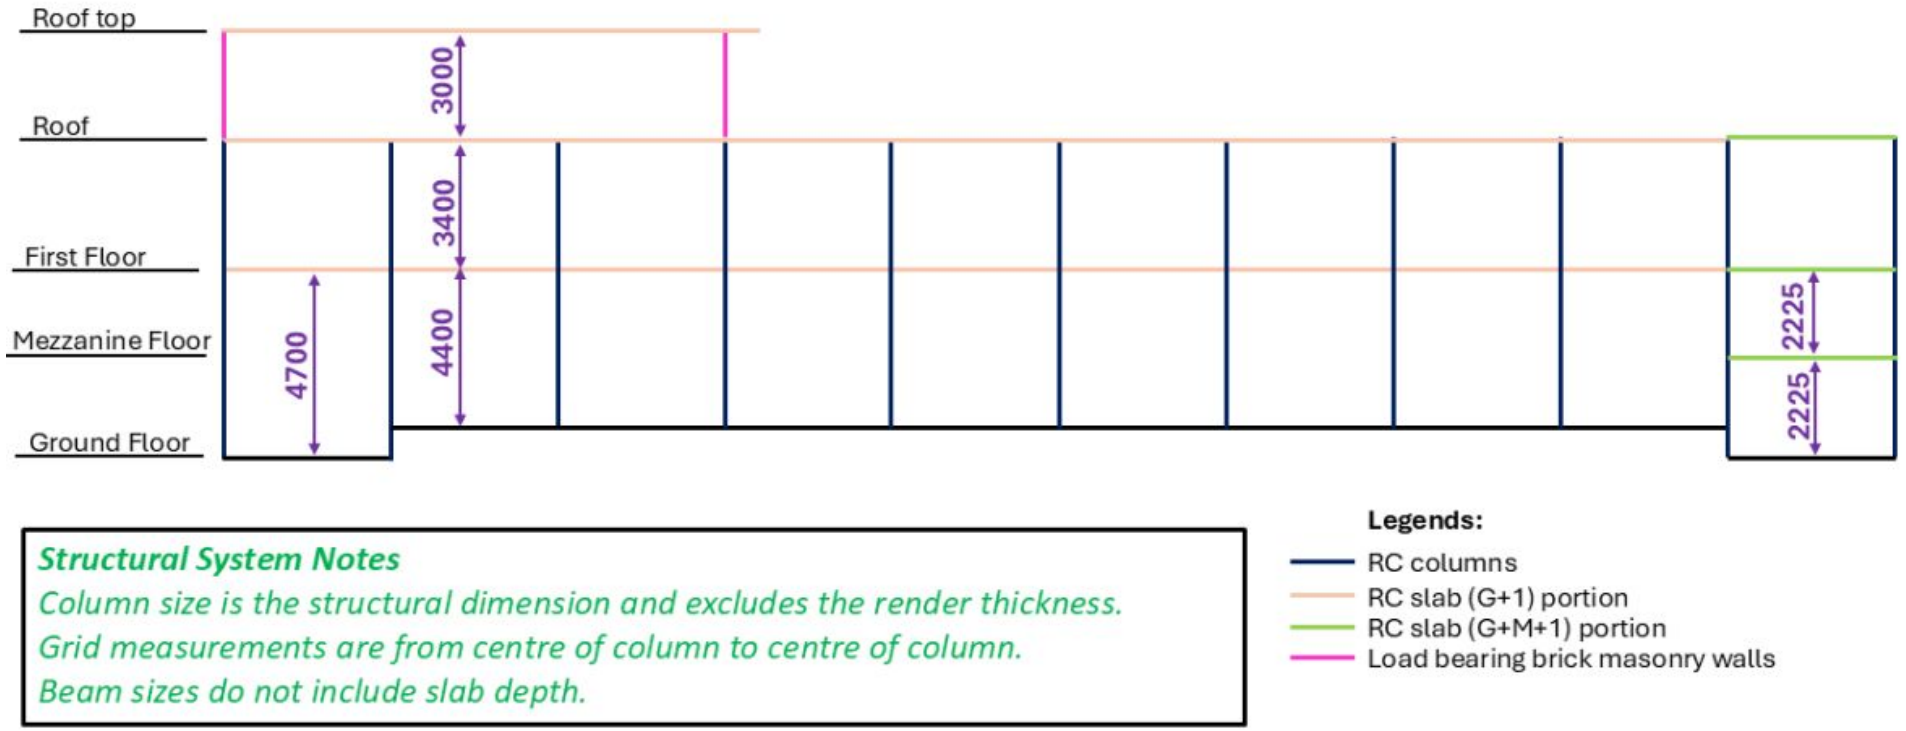


Figure 1.16. Typical section of main building

3. Documentation

We were presented with incomplete site layout plan and stability certificate(expired) at the factory.

Table 2 - Documentation

Building	Site layout	Approved layout / permit	Geotech report	Design drawings	As-built drawings	Loading plan	Stability certificate	Inspection reports	Materials testing
Main Building	Yes (Incomplete)	Yes (Incomplete)	No	No	No	No	Yes (Expired)	No	No

4. Structural Safety Measures

During our structural site inspection of Select Enterprise, a number of structural issues were identified.

It is essential to address these structural safety issues promptly to enhance safety and compliance within Select Enterprise. Each issue should be carefully evaluated, and the recommendations provided in this report should be followed diligently to rectify these concerns. The safety and well-being of the factory's employees depend on these corrective actions. Where issues are identified in the report, they are grouped by topic, not in order of importance. Please note that these actions should be completed as soon as practically possible and certainly within the timeframe noted.

Recommendations in this report are prioritized as follows:

Immediate: These recommendations address safety and compliance concerns that require immediate attention.

Medium term (within approx. 6-weeks): Recommendations of high importance but needing slightly more time to implement.

Longer term (within approx. 6-months): Important recommendations that require a longer period to fully implement or that enhance long-term safety and efficiency.

Table 3: Summary of issues by building

Building	Potential Overstress	Structural system	Cracking	Loading	Other damage & defects	Structural documentation
Main Building	-	-	-	-	Health and safety issues – Unprotected opening at front side of lift	Lack of safe load plans. Documentation Unavailable

5. Remediation Support

5.1 Engineering Support

Some items in the Corrective Action Plan (CAP) will require remediation by a qualified engineer. Please refer to the remediation plan for guidance on which tasks can be completed using internal resources and which require engineering support. F-202604-064569

Timeline	Remediation Plan
Medium Term CAP-0076218	Factories should begin remediation of CAP items—such as surface cracks or non-structural repairs—using internal resources, where available. For remediation based on engineering assessments, detailed engineering assessments, or structural strengthening, engagement of a qualified Structural Engineer is required.

6. Other Damage/Defects

6.1 Health and Safety

This refers to main building.
An unprotected opening is present at the front side of the lift, which poses a risk of potential injury due to slip, trip, or fall. F-202604-064568

Timeline	Remediation Plan
Immediate CAP-0076217	Provide adequate protection at the front side of lift.



Figure 2.1 - Main Building - Identified location of unportected opening at lift front side



Figure 2.2 - Main Building - Unportected opening at lift front side

7. Structural Documentation

7.1 Documentation unavailable

As-built architectual drawings of mezzanine floor and structural drawings of the main building were not available. F-202603-063802

Timeline	Remediation Plan
Longer Term CAP-0074584	Building Structural Engineer to carry out on-site survey, collect information and produce accurate and complete as built documentation.

7.2 Lack of safe load plans

No safe load plans were posted on any floors of main building. F-202603-063803

Timeline	Remediation Plan
Longer Term CAP-0074585	Building structural engineer to review design documentation to confirm load capacity of the structure.
Longer Term CAP-0074586	Develop safe load plans and submit to Pakistan Accord for review.
Longer Term CAP-0074587	Factory to post safe load plans on each floor.

8. Assessment Limitations and Assumptions

The information in this report was obtained during an inspection of the facility and based on information provided by factory management. It has not been possible to provide independent verification for all the information and data collected, and therefore, the Accord cannot accept general responsibility for omissions or errors arising from inaccuracies in this report from the information obtained.

The findings and recommendations in this report are not intended to imply, guarantee, ensure or warrant compliance with any government regulations. Additionally, the results do not imply in any way that compliance with the findings or recommendations as stated in this report will eliminate all hazards, risks or exposures or that hazards, risks or exposures not referred to in this report do not exist. Compliance with the findings and recommendations stated in this report does not relieve the factory owner from obligation to comply with specific project requirements, industry standards, or the provisions of any local government regulations.

Except as otherwise noted within this report, other systems or services were not viewed or tested during the assessment and are therefore similarly excluded from this report. We have not assessed any parts of the structure / building fabric / services which are covered, unexposed or inaccessible and we are therefore unable to report that any such part of the property is free from defect.

The observations in this report are based on the engineering judgement of the engineer at the time of the inspection.
